



Project Office
RFK Stadium Lot 6

C St NE Implementation
DC CONTRACT NO. DCKA-2020-C-0056
FAP No.: CM- 2020 (018)

CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT

08/30/2021 – 09/03/2021

Project Website: www.cstne.com

1. EXECUTIVE SUMMARY

Project Description:

Work under this contract consists of improving the existing streetscape and safety for pedestrians and cyclists. The project plans to mill and overlay the pavement surface, reconstruct sidewalks as needed, and install bulb-outs and bus pads, crosswalks, pavement marking and wheelchair ramps. Streetlights, traffic signals and drainage structures will be upgraded. Other design elements considered for the project are LID elements and intersection improvements. The project will upgrade the bike facilities from bike lanes to protected bike lanes, add more pedestrian crossings, and ensure the street complies with the Americans with Disabilities Act (ADA).

This project is 83% Federally Funded and 17% District-Funded. DDOT selected Anchor construction corporation. as the contractor and awarded the \$15,995,763.50 contract on February 17th, 2021. DDOT issued notice to proceed with contract work to Anchor construction corporation with work to begin on April 26th, 2021 and a substantial completion date of September 28th, 2022

Jacobs is providing Construction Management and Inspection services. DDOT issued a task order to Jacobs on February 12th, 2021 that will expire on October 15th, 2022.

2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Work this week was performed during the day on date, August 30th, 2021 thru date September 3rd, 2021. Work included the CM Agent Team organizing, chairing, and participating in meetings with DDOT, Anchor Construction, WGL, creating and revising meeting minutes, reviewing IDR's, reviewing design plans, reviewing specifications, reviewing RFI's, reviewing submittals, updating submittal and RFI logs, reviewing the monthly schedule update, reviewing quantities, drafting correspondence on DDOT's behalf, and answering various DDOT and Contractor queries.

The Contractor performed the following construction activities this week.

Monday 08/30/2021

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 19th – S&J
 - Excavate for 15" RCP between M6-10 and I7-3
- C St NE & 18th – Grate Line
 - Excavate and place 18" RCP between M6-3 and M6-4
- C St NE & 21st – Anchor
 - Place #57 stone bedding and 15" RCP between M8-4 and I8-7

Tuesday 08/31/2021

CM

- Verified & inspected Contractor work activities and tested concrete

Contractor

- C St NE & 19th – S&J
 - Temporary backfill of 15" RCP between M6-10 and I7-3
- C St NE & 18th – Grate Line
 - Excavate and place 18" RCP between M6-3 and M6-4



- C St NE & 21st – Anchor
 - Place concrete for 15" RCP cradle between M8-4 and I8-7

Wednesday 09/01/2021

CM

- Verified & inspected Contractor work activities

Contractor

- RFK Laydown Yard – Anchor
 - Receive drainage structures
 - Perform maintenance on trench shields

Thursday 09/02/2021

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 19th – S&J
 - Verify and adjust slope of 15" RCP between M6-10 and I7-3
- C St NE & 18th – Grate Line
 - Connect 18" RCP to M6-4, place #57 stone around 18" RCP, backfill trench with RC-6
- C St NE & 21st – Anchor
 - Backfill 15" RCP between I8-7 and M8-4 with RC-6
- 21st & 22nd – Anchor
 - Excavate and place inlet I8-5

Friday 09/03/2021

CM

- Verified & inspected Contractor work activities and tested concrete


Contractor

- C St NE & 19th – S&J
 - Place concrete for 15" RCP cradle between M6-10 and I7-3
- C St NE & 18th – Grate Line
 - Backfill 15" RCP between M6-3 and M6-4 with RC-6
- C St NE & 21st – Anchor
 - Backfill 15" RCP between I8-7 and M8-4 with RC-6
- 21st & 22nd – Anchor
 - Backfill inlet I8-5 with RC-6


3. PHOTOS OF WORK PERFORMED THIS PERIOD



C St NE & 19th St – Excavation for M6-10 to I7-3

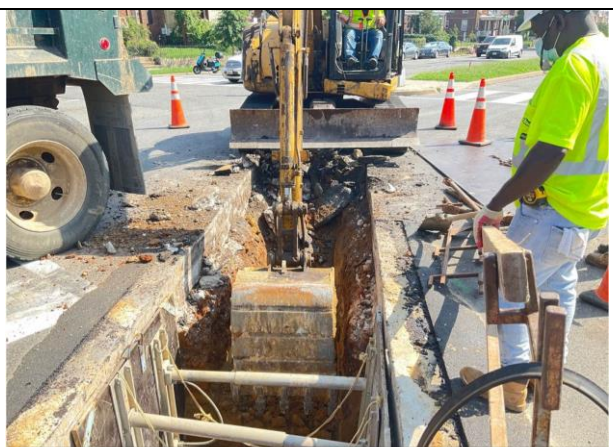


C St NE & 18th St – Trench for RCP between M6-3 and M6-4

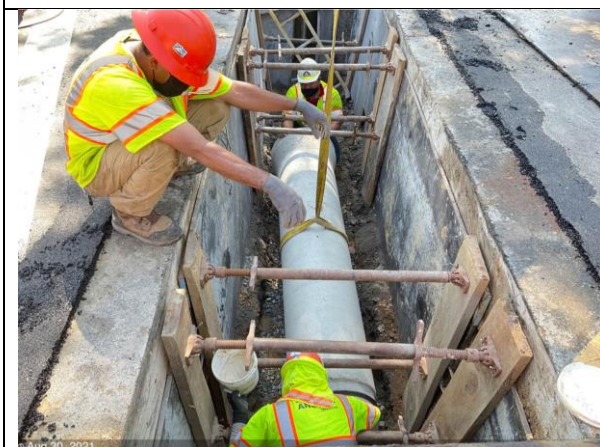

C St NE & 21st St – 15" RCP between M8-4 and I8-7




C St NE & 19th St – Excavation for M6-10 to I7-3

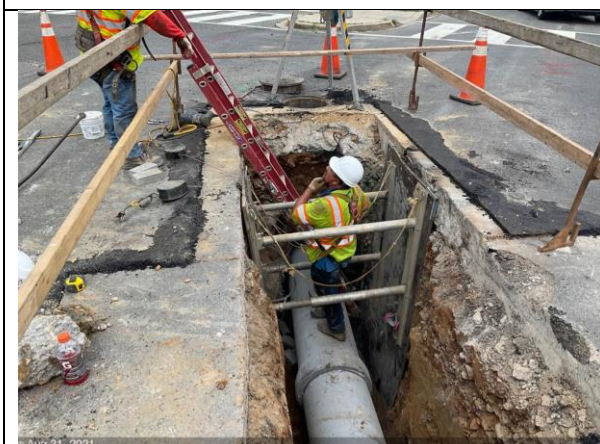

C St NE & 18th St – Place 18" RCP between M6-3 and M6-4



C St NE & 21st St – 15" RCP cradle between M8-4 and I8-7

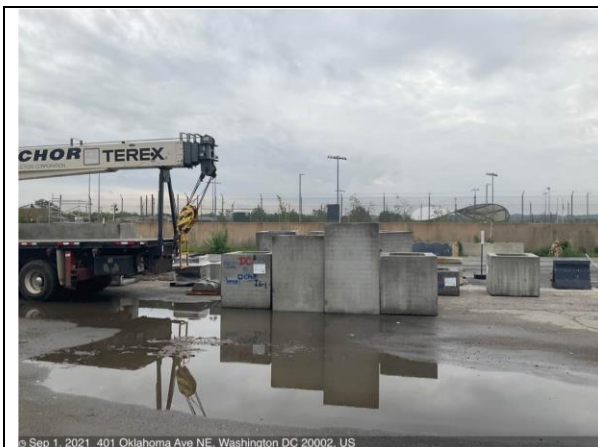


© Sep 1, 2021 401 Oklahoma Ave NE, Washington DC 20002, US

RFK Laydown Yard – Drainage Structure Delivery



© Sep 1, 2021

RFK Laydown Yard – Trench shield maintenance

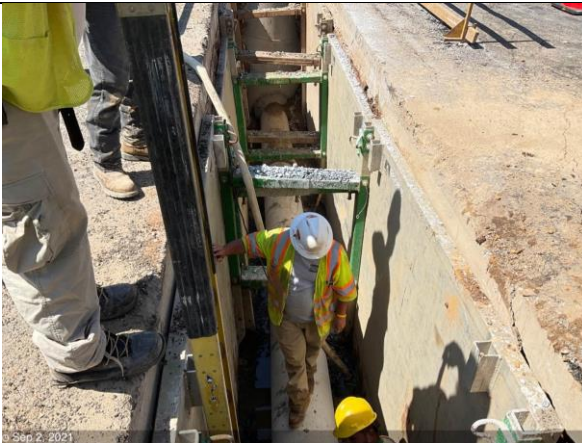

© Sep 2, 2021

C St NE & 19th St – Verify pipe slope for M6-10 to I7-3



© Sep 2, 2021

C St NE & 18th St – Place 18" RCP between M6-3 and M6-4



© Sep 2, 2021 22nd St NE, Washington DC 20003, US

C St NE & 21st – 15" RCP backfill between I8-7 to M8-4



© Sep 2, 2021 22nd St NE, Washington DC 20003, US

21st & 22nd St – I8-5 placement



C St NE & 19th St – Place concrete for 15" RCP cradle between M6-10 and I7-3



C St NE & 18th St – Backfill 18" RCP between M6-3 and M6-4



C St NE & 21st – 15" RCP backfill between I8-7 to M8-4



21st & 22nd St – Backfill I8-5
